

SECTION 00806

CHANGE ORDER

No. One (1)

DATE OF ISSUANCE November 5, 2019

EFFECTIVE DATE _____

OWNER St. Charles Parish Government

CONTRACTOR Hard Rock Construction, LLC

Contract: Highway 90 Sinkhole Remediation

Project: _____

OWNER's Contract No. P180501

ENGINEER's Contract No. _____

ENGINEER T. Baker Smith, LLC

You are directed to make the following changes in the Contract Documents:

Description:

1. Delete the Following Work Items:

N/A

Total of Deducted Items = *(-\$0.00)*

2. Add the Following Work Items:

N/A

Total of Deducted Items = *(-\$0.00)*

3. Revise the Following Work Item Quantities:

- a. 202-02-06100: *Removal of Concrete Walks and Drives*

The quantity is to be changed from 322 SQYDs to 606.0 SQYDs. *(+\$2,840.00)*

- b. 706-02-00200: *Concrete Drive (6" Thick)*

The quantity is to be changed from 346 SQYDs to 606.0 SQYDs. *(+\$15,600.00)*

- c. NS-600-00220: *Saw Cutting Portland Cement Concrete Pavement*

The quantity is to be changed from 2,754 INFT to 5,068 INFT. *(+\$2,314.00)*

Total of Change in Work Items Quantity = *(+\$20,754.00)*

Reason for Change Order: List a reason for each Line Item listed above. *See attached example on how to fill in this information*

1. Deleted Work Items

- a. N/A

2. Add Work Items

- a. N/A

3. Revise Work Item Quantities

- a. Installed quantities for Pay Items Nos. 202-02-06100, 706-02-00220 and NS-600-00220 over ran the contract quantities due to changes in the field once construction started. These changes are necessary to balance contract quantities with installed quantities.

Attachments: (List documents supporting change)

Fully Executed Work Directive

CHANGE IN CONTRACT PRICE:
Original Contract Price \$163,955.40
Net Increase (Decrease) from previous Change Orders No. <u> </u> to <u> </u> : \$ 0.00
Contract Price prior to this Change Order: \$ 163,955.40
Net increase (decrease) of this Change Order: \$20,754.00
Contract Price with all approved Change Orders: \$ 184,709.40

CHANGE IN CONTRACT TIMES:
Original Contract Times: 45 Days Substantial Completion: <u>October 17, 2019</u> Ready for final payment: <u>45 Days</u> (days or dates)
Net change from previous Change Orders No. <u> </u> to No. <u> </u> : Substantial Completion: <u>October 17, 2019</u> Ready for final payment: <u>45 Days</u> (days)
Contract Times prior to this Change Order: Substantial Completion: <u>October 17, 2019</u> Ready for final payment: <u>45 Days</u> (days or dates)
Net increase (decrease) this Change Order: Substantial Completion: <u>10 days</u> Ready for final payment: <u>45 Days</u> (days)
Contract Times with all approved Change Orders: Substantial Completion: <u>October 27, 2019</u> Ready for final payment: <u>45 Days</u> (days or dates)

RECOMMENDED:

APPROVED:

ACCEPTED:

By: _____
ENGINEER (Authorized Signature)

By: _____
OWNER (Authorized Signature)

By: _____
CONTRACTOR(Authorized Signature)

Date: _____

Date: _____

Date: _____

SECTION 00805

WORK CHANGE DIRECTIVE

No. One (1)

DATE OF ISSUANCE September 17, 2019 EFFECTIVE DATE _____

OWNER St. Charles Parish Government

CONTRACTOR Hardrock Construction, LLC

Contract: Highway 90 Sinkhole Remediation

Project: _____

OWNER's Contract No. P180501 ENGINEER's Contract No. _____

ENGINEER T. Baker Smith, LLC

Contractor is directed to proceed promptly with the following change(s):

Description: Contractor is directed to remove and replace existing concrete pavement along project alignment at Sinkhole No. 2 location. Contractor to remove and replace a section of existing concrete pavement 6' wide x 200' long on North side of pipe trench and 8' wide x 200' long on South side of pipe trench. Contractor to saw cut concrete to provide a smooth transition between existing concrete and new proposed concrete. Adverse weather delays and days for additional work are included.

Attachments: (List documents supporting change) Untitled Map

Purpose for Work Change Directive:

Directive to proceed promptly with the Work described herein, prior to agreeing to changes on Contract Price and Contract Time, is issued due to: (check one)

- ☐ Non-agreement on pricing of proposed change.
☒ Necessity to proceed for schedule or other project reasons.

Estimated Change in Contract Price and Contract Times (non-binding, preliminary):

Contract Price: \$ 24,369.78 [increase] [~~decrease~~]

Contract Time Ten (10) days [increase] [~~decrease~~]

Basis of estimated change in Contract Price:


- ☐ Lump Sum ☒ Unit Price
☐ Cost of the Work ☐ Other

Recommended:	Limited Authorization By*:	Received:
By: <u>[Signature]</u>	By: <u>[Signature]</u>	By: <u>[Signature]</u>
Engineer (Authorized Signature)	Owner's Representative*	Contractor (Authorized Signature)
Title: <u>Sr. Construction Mgr</u>	Title: <u>Donor</u>	Title: <u>Project Manager</u>
Date: <u>9/17/2019</u>	Date: <u>9/17/19</u>	Date: <u>9/18/2019</u>

*Owner's Representative is not authorized to finalize a Change Order nor does the Work Change Directive substitute the Change Order process as more fully set out in the General Conditions of the Construction Contract.

Approved by Funding Agency (if applicable)

By: _____ Date: _____
Title: _____

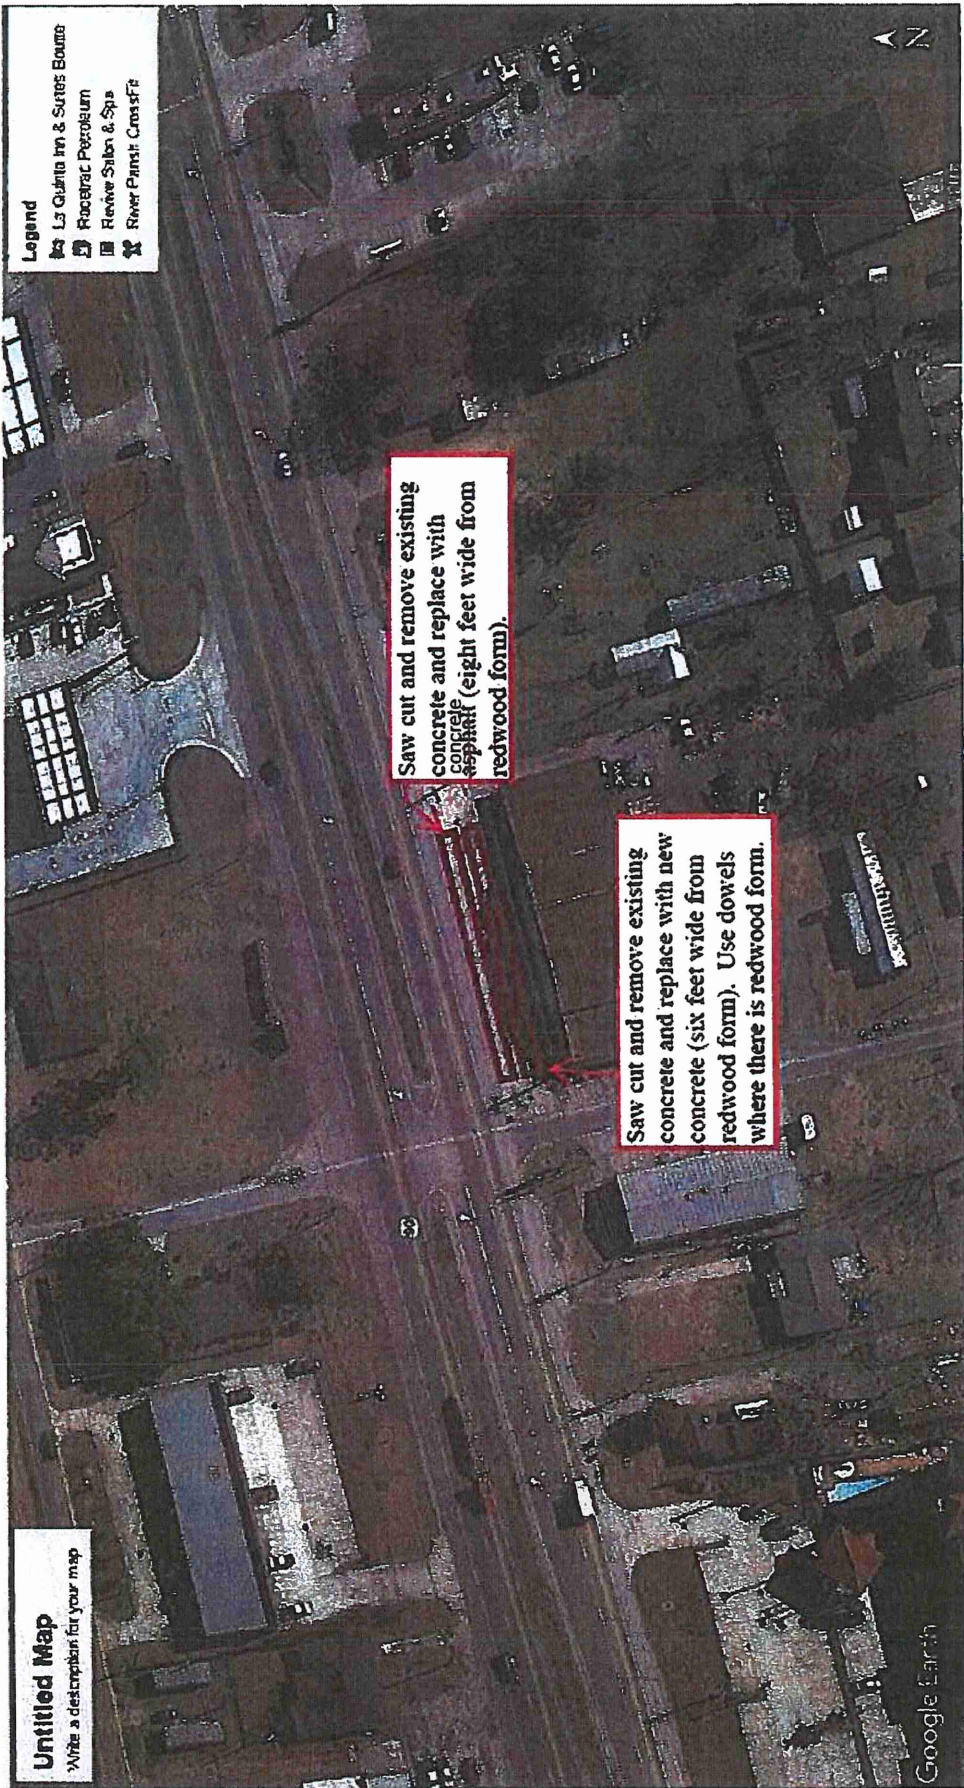

- Legend
- La Quinta Inn & Suites Bldg
 - RaceTrac Petroleum
 - Review Sign & Spa
 - River Pointe CrossFit

Untitled Map
Write a description for your map

Saw cut and remove existing concrete and replace with concrete asphalt (eight feet wide from redwood form).

Saw cut and remove existing concrete and replace with new concrete (six feet wide from redwood form). Use dowels where there is redwood form.
